


Contingency Curve

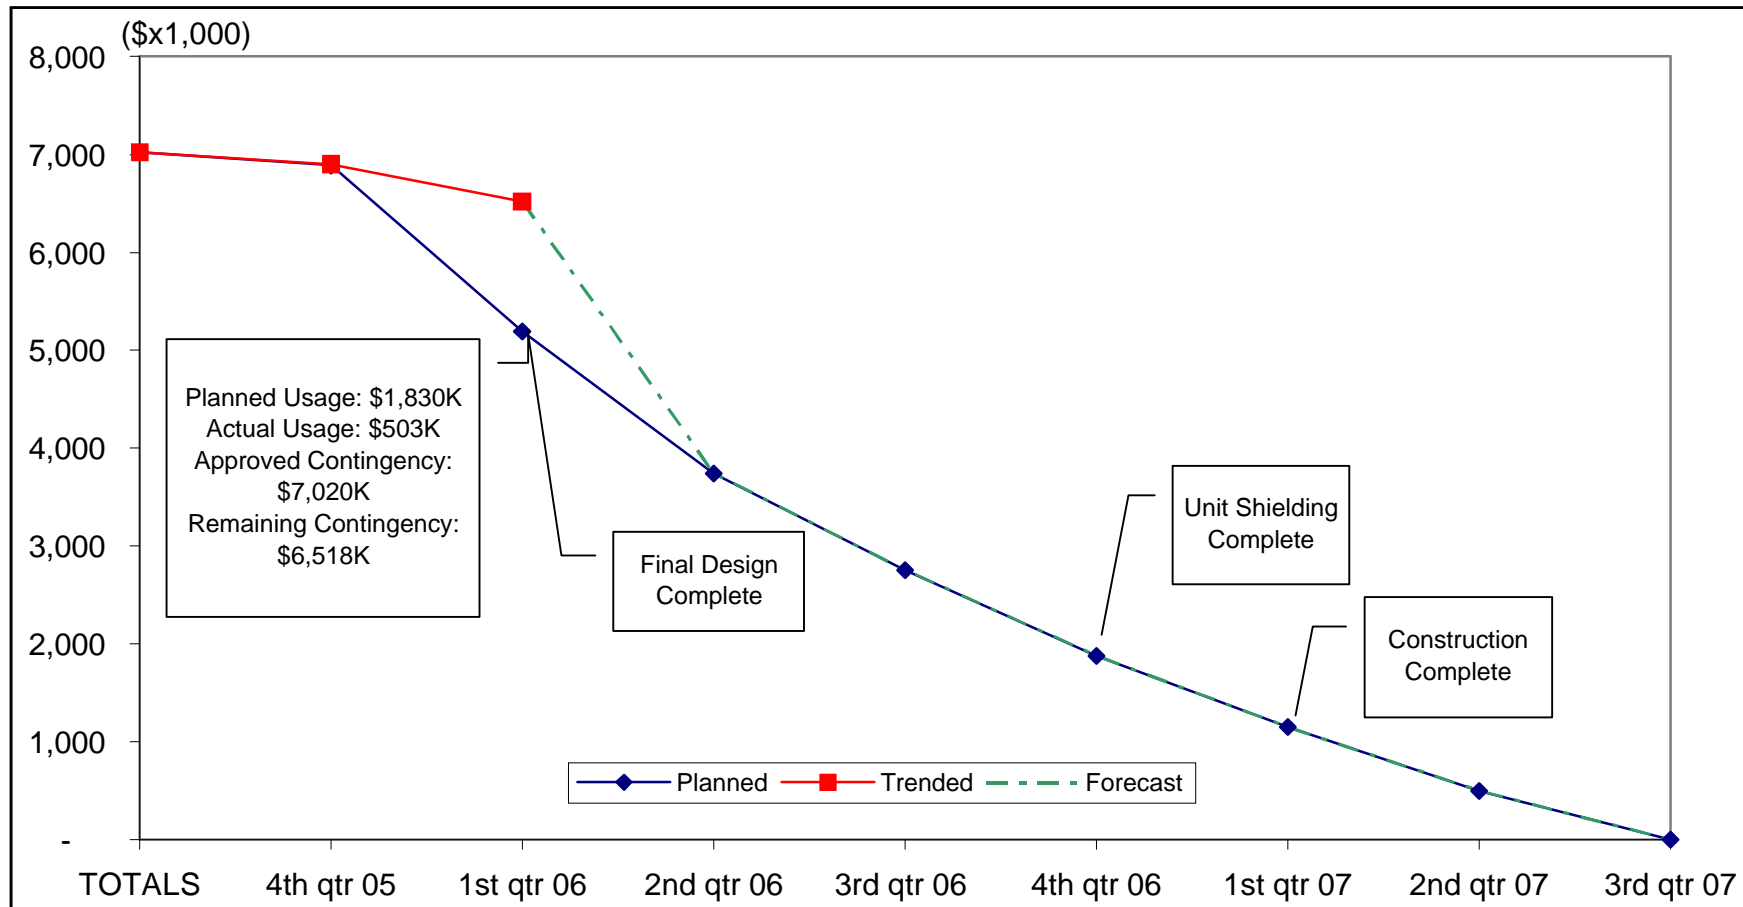

Risk-O-Meter Summary

Risk Priority	Risk #	Risk Title	Risk Level	Handling Strategy	Residual Cost \$K		Closed	Stable	Minor Concern	Major Concern	Status/Comments	Trigger Point
					ML	WC						
1		Interface to Facility Missions	H	Reduce	\$1,500	\$3,000						
2		Multiple Contractors	H	Reduce	\$1,500	\$3,000						
3		Funding Profile Not Met	H	Reduce	\$1,500	\$5,000						
4		Unidentified Facility/System Defects Cause Scope Growth	H	Reduce	\$1,000	\$2,000						
5		Scope Growth Inside Scope Boundary Limits	H	Reduce	\$1,000	\$2,000						Beginning construction while still completing some design of interfaces
6		Equipment and Commodities Costs Increase due to Raw Materials Price Increases	H	Reduce	\$1,000	\$3,000						Placement of purchase orders impacted commodities
7		Serious Injuries to Project Personnel	H	Reduce	\$250	\$500						Safety program in place. Still a concern with the start of major construction activities.
8		Technology Concept Not Proven	H	Reduce	\$500	\$1,000						
9		Poor Supplier Performance	H	Reduce	\$2,500	\$500						Progress check points in major procurements or subcontracts
10		Specified Plant Performance Not Met	H	Reduce	\$250	\$500						

LEGEND	
	Risk has been closed
	Working, no issues at this time
	Minor concern
	Major concern
(N)	New Risk
